PROPERTY CHANGES SINCE JUNE 30. 1918.
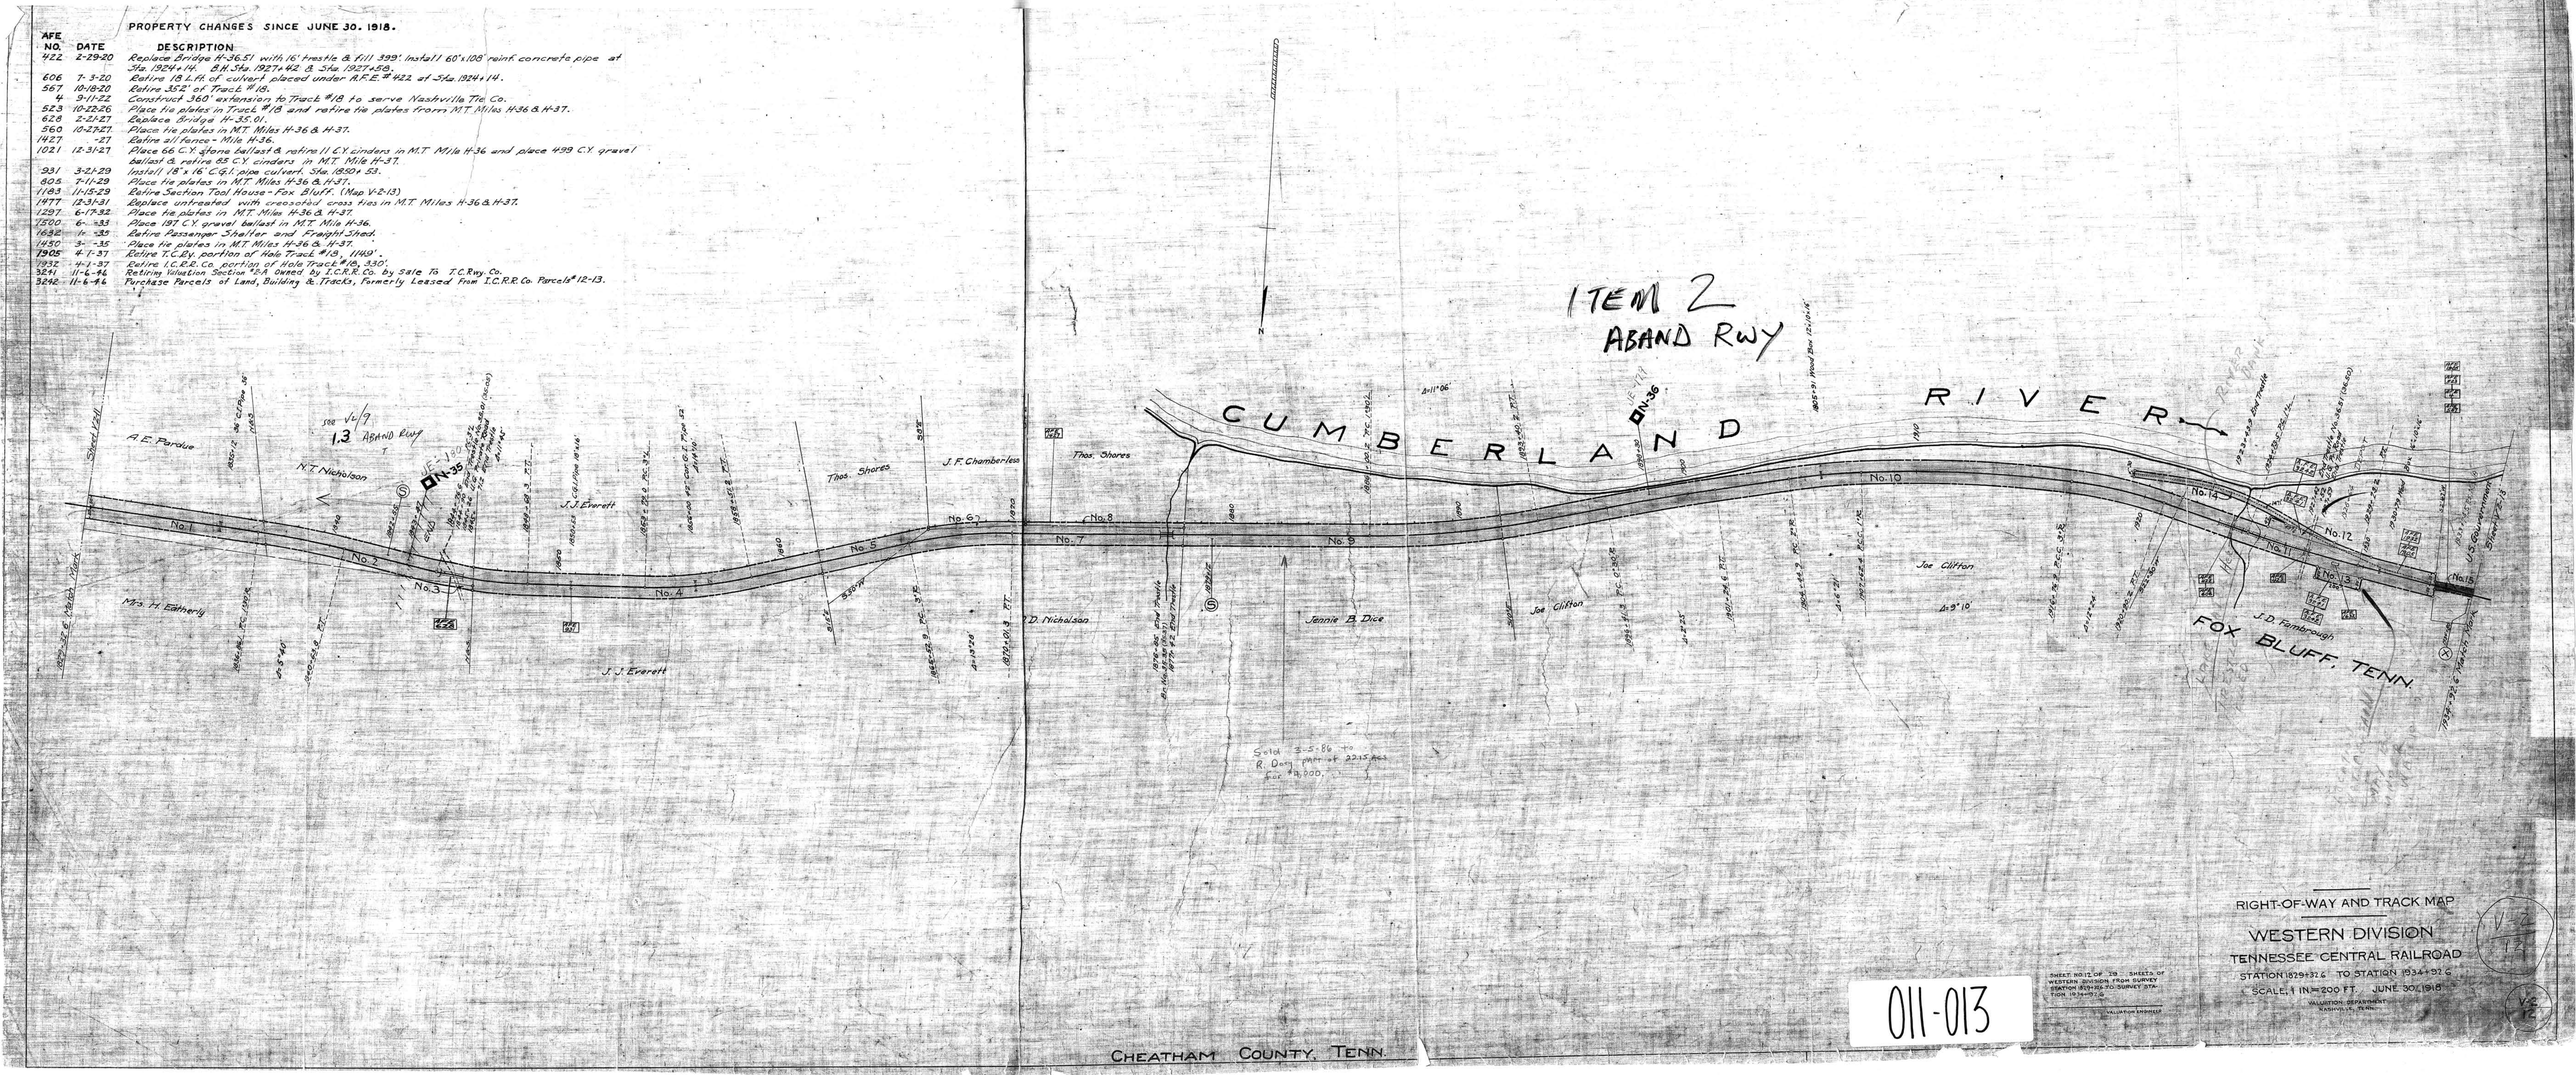
AFE NO.	DATE	DESCRIPTION
422	2-29-20	Replace Bridge H-36.51 with 16' trestle & fill 399'. Install 60"x108' reinf. concrete pipe at Sta. 1924+14. B.H. Sta. 1927+42. & Sta. 1927+58.
606	7-3-20	Retire 18 L.ft. of culvert placed under A.F.E. #422 at Sta. 1924+14.
567	10-18-20	Retire 352' of Track #18.
4	9-11-22	Construct 360' extension to Track #18 to serve Nashville Tie Co.
523	10-22-26	Place tie plates in Track #18 and retire tie plates from M.T. Miles H-36 & H-37.
628	2-21-27	Replace Bridge H-35.01.
560	10-27-27	Place tie plates in M.T. Miles H-36 & H-37.
1427	-27	Retire all fence - Mile H-36.
1021	12-31-27	Place 66 C.Y. stone ballast & retire 11 C.Y. cinders in M.T. Mile H-36 and place 499 C.Y. gravel ballast & retire 85 C.Y. cinders in M.T. Mile H-37.
931	3-21-29	Install 18" x 16' C.G.I. pipe culvert. Sta. 1950+53.
805	7-11-29	Place tie plates in M.T. Miles H-36 & H-37.
1183	11-15-29	Retire Section Tool House - Fox Bluff. (Map V-2-13)
1477	12-31-31	Replace untreated with creosoted cross ties in M.T. Miles H-36 & H-37.
1297	6-17-32	Place tie plates in M.T. Miles H-36 & H-37.
1500	6- -33	Place 197 C.Y. gravel ballast in M.T. Mile H-36.
1682	1- -35	Retire Passenger Shelter and Freight Shed.
1430	3- -35	Place tie plates in M.T. Miles H-36 & H-37.
1905	4-17-37	Retire T.C.Ry. portion of Hole Track #19. 1149'.
1932	4-1-37	Retire I.C.R.R. Co. portion of Hole Track #19. 330'.
3241	11-6-46	Retiring Valuation Section "B-A" owned by I.C.R.R. Co. by Sale to T.C.Ry. Co.
3242	11-6-46	Purchase Parcels of Land, Building & Tracks, Formerly Leased from I.C.R.R. Co. Parcels # 12-13.
