PROPERTY CHANGES SINCE DEC. 15, 1923.
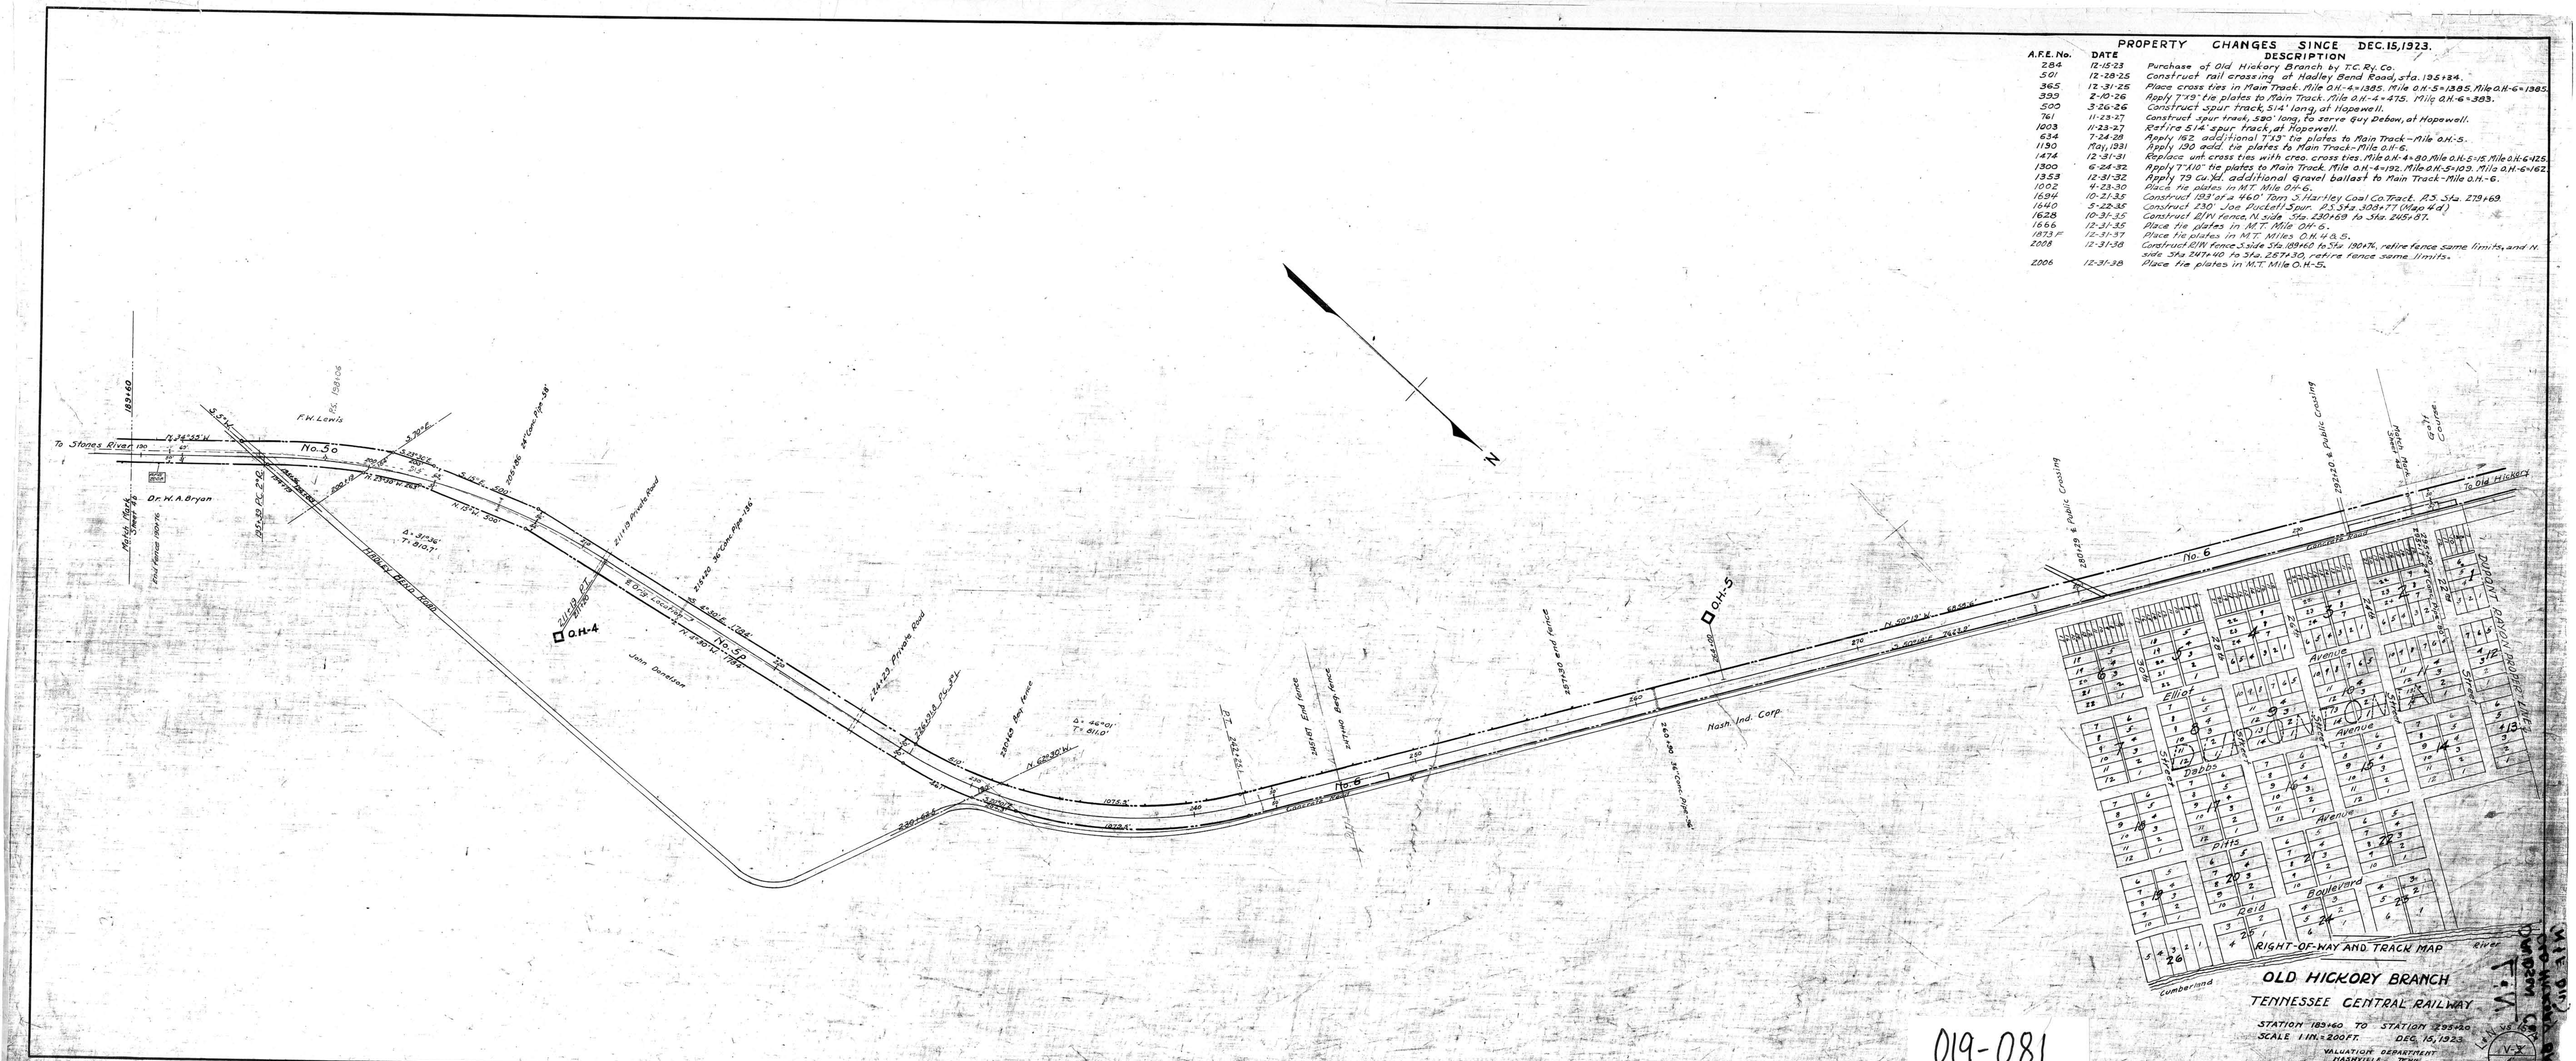
A.F.E. No.	DATE	DESCRIPTION
284	12-15-23	Purchase of Old Hickory Branch by T.C. Ry. Co.
501	12-28-25	Construct rail crossing at Hadley Bend Road, Sta. 135+34.
365	12-31-25	Place cross ties in Main Track. Mile O.H.-4=1385. Mile O.H.-5=1385. Mile O.H.-6=1385.
399	2-10-26	Apply 7"x9" tie plates to Main Track. Mile O.H.-4=475. Mile O.H.-6=383.
500	3-26-26	Construct spur Track, 514' long, at Hopewell.
761	11-23-27	Construct spur track, 320' long, to serve Guy Debon, at Hopewell.
1003	11-23-27	Retire 514' spur track, at Hopewell.
634	7-24-28	Apply 162 additional 7"x13" tie plates to Main Track—Mile O.H.-5.
1130	May, 1931	Apply 120 add. tie plates to Main Track—Mile O.H.-6.
1474	12-31-31	Replace unf. cross ties with creo. cross ties. Mile O.H.-4=80. Mile O.H.-5=15. Mile O.H.-6=125.
1300	6-24-32	Apply 7"x10" tie plates to Main Track. Mile O.H.-4=192. Mile O.H.-5=103. Mile O.H.-6=162.
1358	12-31-32	Apply 79 cu. yd. additional gravel ballast to Main Track—Mile O.H.-6.
1002	4-23-30	Place tie plates in M.T. Mile O.H.-6.
1694	10-21-35	Construct 193' of a 460' Tom S. Hartley Coal Co. Track. R.S. Sta. 279+69.
1640	5-22-35	Construct 230' Joe Puckett Spur. P.S. Sta. 308+77 (Map 4d)
1628	10-31-35	Construct 20'N fence, N. side Sta. 230+69 to Sta. 245+87.
1666	12-31-35	Place tie plates in M.T. Mile O.H.-6.
1873	12-31-37	Place tie plates in M.T. Miles O.H.-4 & 5.
2058	12-31-38	Construct 20'N fence, S. side Sta. 189+60 to Sta. 190+76, retire fence same limits, and N. side Sta. 247+40 to Sta. 267+30, retire fence same limits.
2006	12-31-38	Place tie plates in M.T. Mile O.H.-5.
